

COMMITTEE OF THE WHOLE - FEBRUARY 1, 2011

REQUEST FOR ADDITIONAL FUNDING T09-452 - 2009 ROAD RESURFACING/REHABILITATION PART III - VARIOUS LOCATIONS WARD 5

Recommendation

The Commissioner of Engineering and Public Works in consultation with the Director of Purchasing Services and the Director of Reserves and Investments recommends;

That additional funds in the amount of \$217,000.00 for Tender T09-452 be approved and funded from Capital Account EN-1729-09, 2009 Pavement Management Program.

Contribution to Sustainability

The rehabilitation of roads undertaken as part of this contract ensures that an acceptable level of service is maintained by the City's infrastructure for the health and well being of its citizens.

Economic Impact

Additional funding in the amount of \$217,000.00 is being allocated to this specific project from the total budget approved in the 2009 Capital Budget. There are sufficient funds in the approved budget, funded from the "Investing in Ontario" Provincial Grant, to pay the final project costs.

Communications Plan

Not Applicable.

Purpose

To obtain Council approval for additional funding required to complete final payment for previously approved Capital Contract T09-452.

Background - Analysis and Options

Contract T09-452, 2009 Road Resurfacing/Rehabilitation – Part III, Various Locations, Capital Account EN-1729-09 was awarded by Council on January 26, 2010, in the amount of \$1,951,561.00, with a contingency allowance of \$200,000.00, plus applicable taxes, funded from "Investing in Ontario" Provincial Grant.

During construction, field staff encountered additional works than what was originally anticipated during tendering of the project. These works included:

- Additional removal and replacement of curb & gutter
- Additional removal and replacement of sidewalks
- Additional restoration of driveways as a result of curb and sidewalk removal
- Additional base asphalt crack repairs

The additional funding request for this project is calculated as follows:

Additional Funding Request (excluding H.S.T.)	\$207,000.00
Non-Refundable Portion of H.S.T. (1.76%)	<u>\$ 3,643.20</u>
Sub-Total	\$210,643.20
Treasury Administration (3%)	<u>\$ 6,319.30</u>
Net Total Cost	\$216,962.50

ROUNDED \$217,000.00

As a result of this work, the associated tender items exceeded the preliminary project estimate amount, and resulted in additional costs of \$217,000.00. All work undertaken was in accordance with Departmental Policies and Procedures.

The additional costs required to complete the above mentioned work is related to roadworks and can be funded within the approved Capital Budget EN-1729-09, 2009 Pavement Management Program.

Relationship to Vaughan Vision 2020/Strategic Plan

In consideration of the strategic priorities related to Vaughan Vision 2020, the recommendations of this report will assist in:

- Pursue Excellence in Service Delivery;
- Enhance and Ensure Community Safety, Health & Wellness; and
- Lead and Promote Environmental Sustainability

This report is consistent with the priorities previously set by Council.

Regional Implications

Not Applicable.

Conclusion

The funds requested are required to pay the contractor the cost of additional work required in the completion of this project. The cost and quantities involved have been verified by Engineering Services staff. It is therefore appropriate to approve the payment of the funds as requested.

Attachments

1. Location Map.

Report prepared by:

Gino Martino, B.A., C. Tech., Engineering Technologist - Capital, ext. 3151
Justin Metras, C. Tech., Manager of Construction Services, ext. 3140


Respectfully submitted,

Bill Robinson, P. Eng.
Commissioner of Engineering and Public Works

Jack Graziosi, P. Eng., M. Eng.
Director of Engineering Services

GM:mc

LOCATION MAP

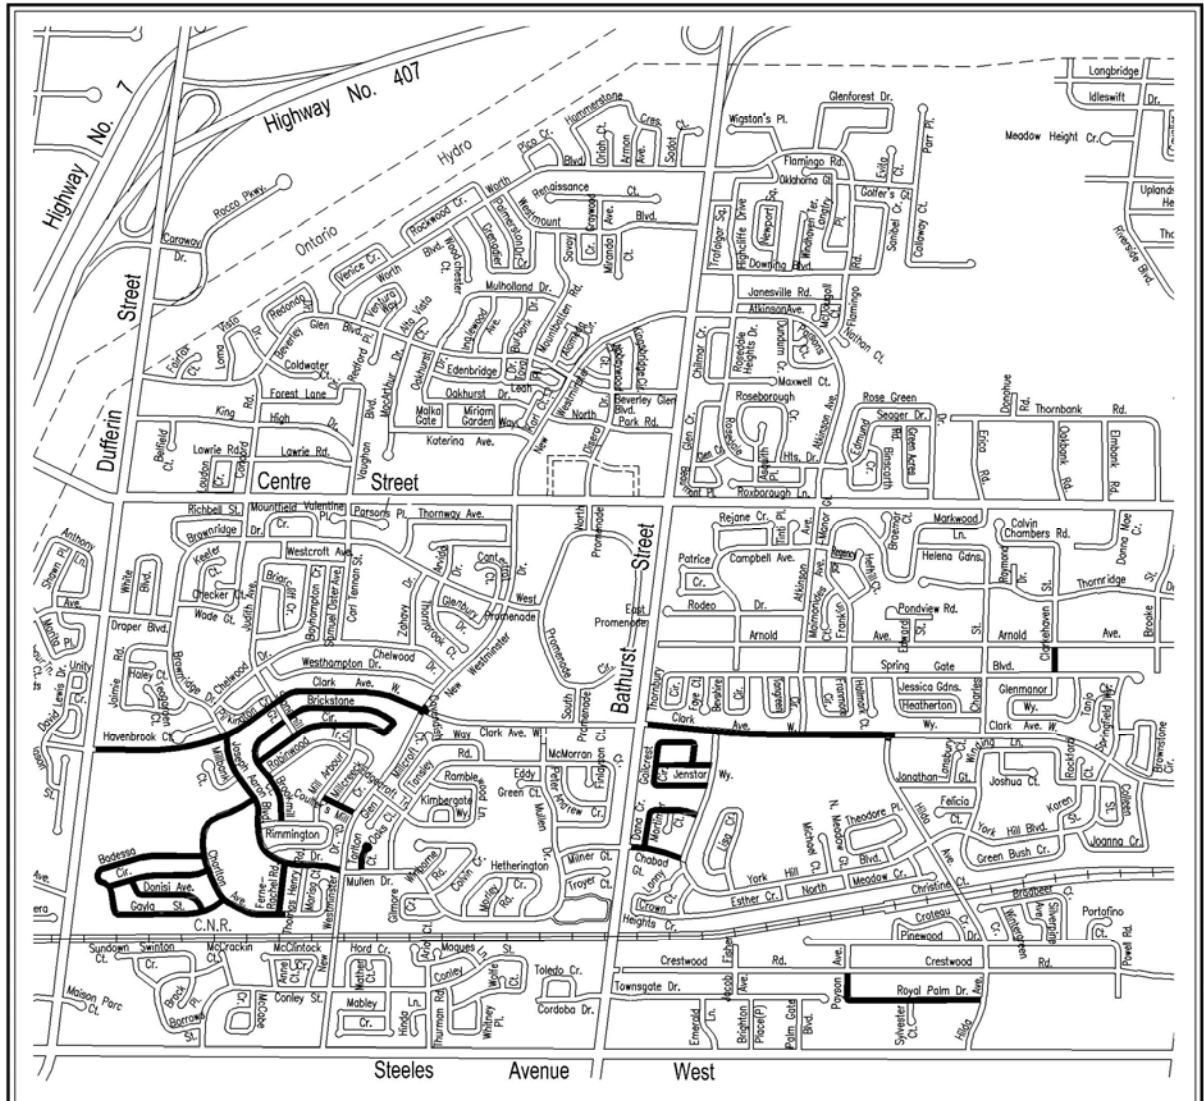


2009 ROAD RESURFACING / REHABILITATION - PART III

VARIOUS LOCATIONS

T09 - 452

LEGEND

 SUBJECT ROADS



NOT TO SCALE
